


| ID | Task Name                                  | Duration       | Start               | Finish              | Predecessors | Resource Names     | 25 | 27 | March 2017 |    |    |    |    |  |  |  |
|----|--------------------------------------------|----------------|---------------------|---------------------|--------------|--------------------|----|----|------------|----|----|----|----|--|--|--|
|    |                                            |                |                     |                     |              |                    | 01 | 03 | 05         | 07 | 09 | 11 | 13 |  |  |  |
| 1  | <b>Self-oriented Solar Mirror</b>          | <b>83 days</b> | <b>Thu 02/03/17</b> | <b>Mon 26/06/17</b> |              |                    |    |    |            |    |    |    |    |  |  |  |
| 2  | <b>Initial planning</b>                    | <b>3 days</b>  | <b>Thu 02/03/17</b> | <b>Mon 06/03/17</b> |              |                    |    |    |            |    |    |    |    |  |  |  |
| 3  | Task allocation                            | 2 days         | Thu 02/03/17        | Fri 03/03/17        |              | Margot             |    |    |            |    |    |    |    |  |  |  |
| 4  | Gantt Chart                                | 1 day          | Fri 03/03/17        | Fri 03/03/17        |              | José               |    |    |            |    |    |    |    |  |  |  |
| 5  | Technical research                         | 3 days         | Thu 02/03/17        | Sun 05/03/17        |              | Jan                |    |    |            |    |    |    |    |  |  |  |
| 6  | Market research                            | 3 days         | Thu 02/03/17        | Sun 05/03/17        |              | Margot, Anna       |    |    |            |    |    |    |    |  |  |  |
| 7  | Initial budget planning                    | 3 days         | Thu 02/03/17        | Sun 05/03/17        |              | Raymond            |    |    |            |    |    |    |    |  |  |  |
| 8  | Purpose definition                         | 1 day          | Mon 06/03/17        | Mon 06/03/17        | 5;6;7        | All                |    |    |            |    |    |    |    |  |  |  |
| 9  | <b>Specific planning</b>                   | <b>36 days</b> | <b>Mon 06/03/17</b> | <b>Mon 24/04/17</b> |              |                    |    |    |            |    |    |    |    |  |  |  |
| 10 | System diagrams                            | 6 days         | Mon 06/03/17        | Mon 13/03/17        |              | Jan                |    |    |            |    |    |    |    |  |  |  |
| 11 | Structural draft                           | 6 days         | Mon 06/03/17        | Mon 13/03/17        |              | José               |    |    |            |    |    |    |    |  |  |  |
| 12 | Design                                     | 10 days        | Tue 14/03/17        | Mon 27/03/17        | 10;11        | Jan                |    |    |            |    |    |    |    |  |  |  |
| 13 | Material research and budget replanning    | 5 days         | Tue 28/03/17        | Mon 03/04/17        |              | Raymond            |    |    |            |    |    |    |    |  |  |  |
| 14 | Complete list of materials                 | 15 days        | Tue 04/04/17        | Mon 24/04/17        | 13           | Margot             |    |    |            |    |    |    |    |  |  |  |
| 15 | <b>Interim</b>                             | <b>26 days</b> | <b>Tue 28/03/17</b> | <b>Tue 02/05/17</b> |              |                    |    |    |            |    |    |    |    |  |  |  |
| 16 | Project management                         | 6 days         | Mon 03/04/17        | Sun 09/04/17        |              | Anna               |    |    |            |    |    |    |    |  |  |  |
| 17 | Eco-efficiency measures for sustainability | 6 days         | Mon 03/04/17        | Sun 09/04/17        |              | José               |    |    |            |    |    |    |    |  |  |  |
| 18 | Ethical and deontological concerns         | 6 days         | Mon 03/04/17        | Sun 09/04/17        |              | Raymond            |    |    |            |    |    |    |    |  |  |  |
| 19 | Upload interim report and presentation     | 10 days        | Tue 28/03/17        | Sun 09/04/17        |              | Anna               |    |    |            |    |    |    |    |  |  |  |
| 20 | Interim presentation                       | 9 days         | Mon 10/04/17        | Thu 20/04/17        | 19           | Margot             |    |    |            |    |    |    |    |  |  |  |
| 21 | Upload refined Interim report              | 8 days         | Fri 21/04/17        | Tue 02/05/17        | 20           | Anna               |    |    |            |    |    |    |    |  |  |  |
| 22 | <b>Construction</b>                        | <b>17 days</b> | <b>Tue 02/05/17</b> | <b>Wed 24/05/17</b> |              |                    |    |    |            |    |    |    |    |  |  |  |
| 23 | Construction hardware                      | 17 days        | Tue 02/05/17        | Wed 24/05/17        |              | José, Raymond      |    |    |            |    |    |    |    |  |  |  |
| 24 | Construction software                      | 17 days        | Tue 02/05/17        | Wed 24/05/17        |              | Jan                |    |    |            |    |    |    |    |  |  |  |
| 25 | <b>Testing</b>                             | <b>13 days</b> | <b>Thu 25/05/17</b> | <b>Mon 12/06/17</b> |              |                    |    |    |            |    |    |    |    |  |  |  |
| 26 | Product testing                            | 8 days         | Thu 25/05/17        | Mon 05/06/17        | 22           | All                |    |    |            |    |    |    |    |  |  |  |
| 27 | Corrections                                | 13 days        | Thu 25/05/17        | Mon 12/06/17        |              | José, Raymond, Jan |    |    |            |    |    |    |    |  |  |  |
| 28 | <b>Final</b>                               | <b>18 days</b> | <b>Thu 01/06/17</b> | <b>Mon 26/06/17</b> |              |                    |    |    |            |    |    |    |    |  |  |  |
| 29 | Final report and presentation upload       | 10 days        | Tue 06/06/17        | Sun 18/06/17        |              | Margot             |    |    |            |    |    |    |    |  |  |  |
| 30 | Movie                                      | 13 days        | Thu 01/06/17        | Sun 18/06/17        |              | Jan                |    |    |            |    |    |    |    |  |  |  |
| 31 | Demonstration                              | 13 days        | Thu 01/06/17        | Sun 18/06/17        |              | Anna               |    |    |            |    |    |    |    |  |  |  |
| 32 | Poster                                     | 13 days        | Thu 01/06/17        | Sun 18/06/17        |              | Margot             |    |    |            |    |    |    |    |  |  |  |
| 33 | Manual                                     | 13 days        | Thu 01/06/17        | Sun 18/06/17        |              | Anna               |    |    |            |    |    |    |    |  |  |  |
| 34 | Leaflet                                    | 13 days        | Thu 01/06/17        | Sun 18/06/17        |              | Margot             |    |    |            |    |    |    |    |  |  |  |
| 35 | Final presentation                         | 4 days         | Mon 19/06/17        | Thu 22/06/17        | 29           | Anna               |    |    |            |    |    |    |    |  |  |  |
| 36 | Finish Wiki                                | 6 days         | Mon 19/06/17        | Mon 26/06/17        |              | Margot             |    |    |            |    |    |    |    |  |  |  |
| 37 | Corrected printed report                   | 3 days         | Thu 22/06/17        | Mon 26/06/17        |              | Anna               |    |    |            |    |    |    |    |  |  |  |

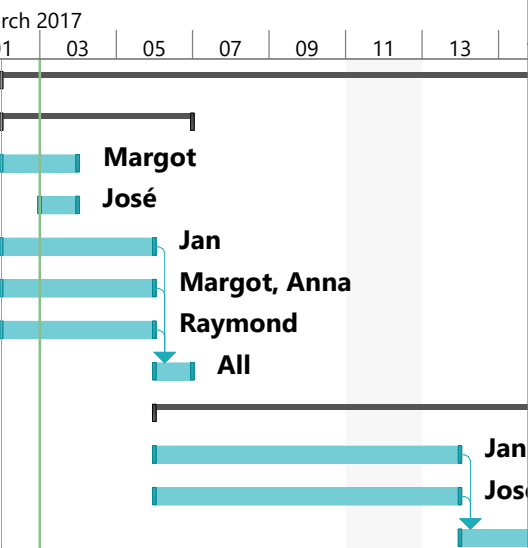

Project: TEAM 3-EPS  
Date: Fri 03/03/17

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline


Progress

Manual Progress

Page 1

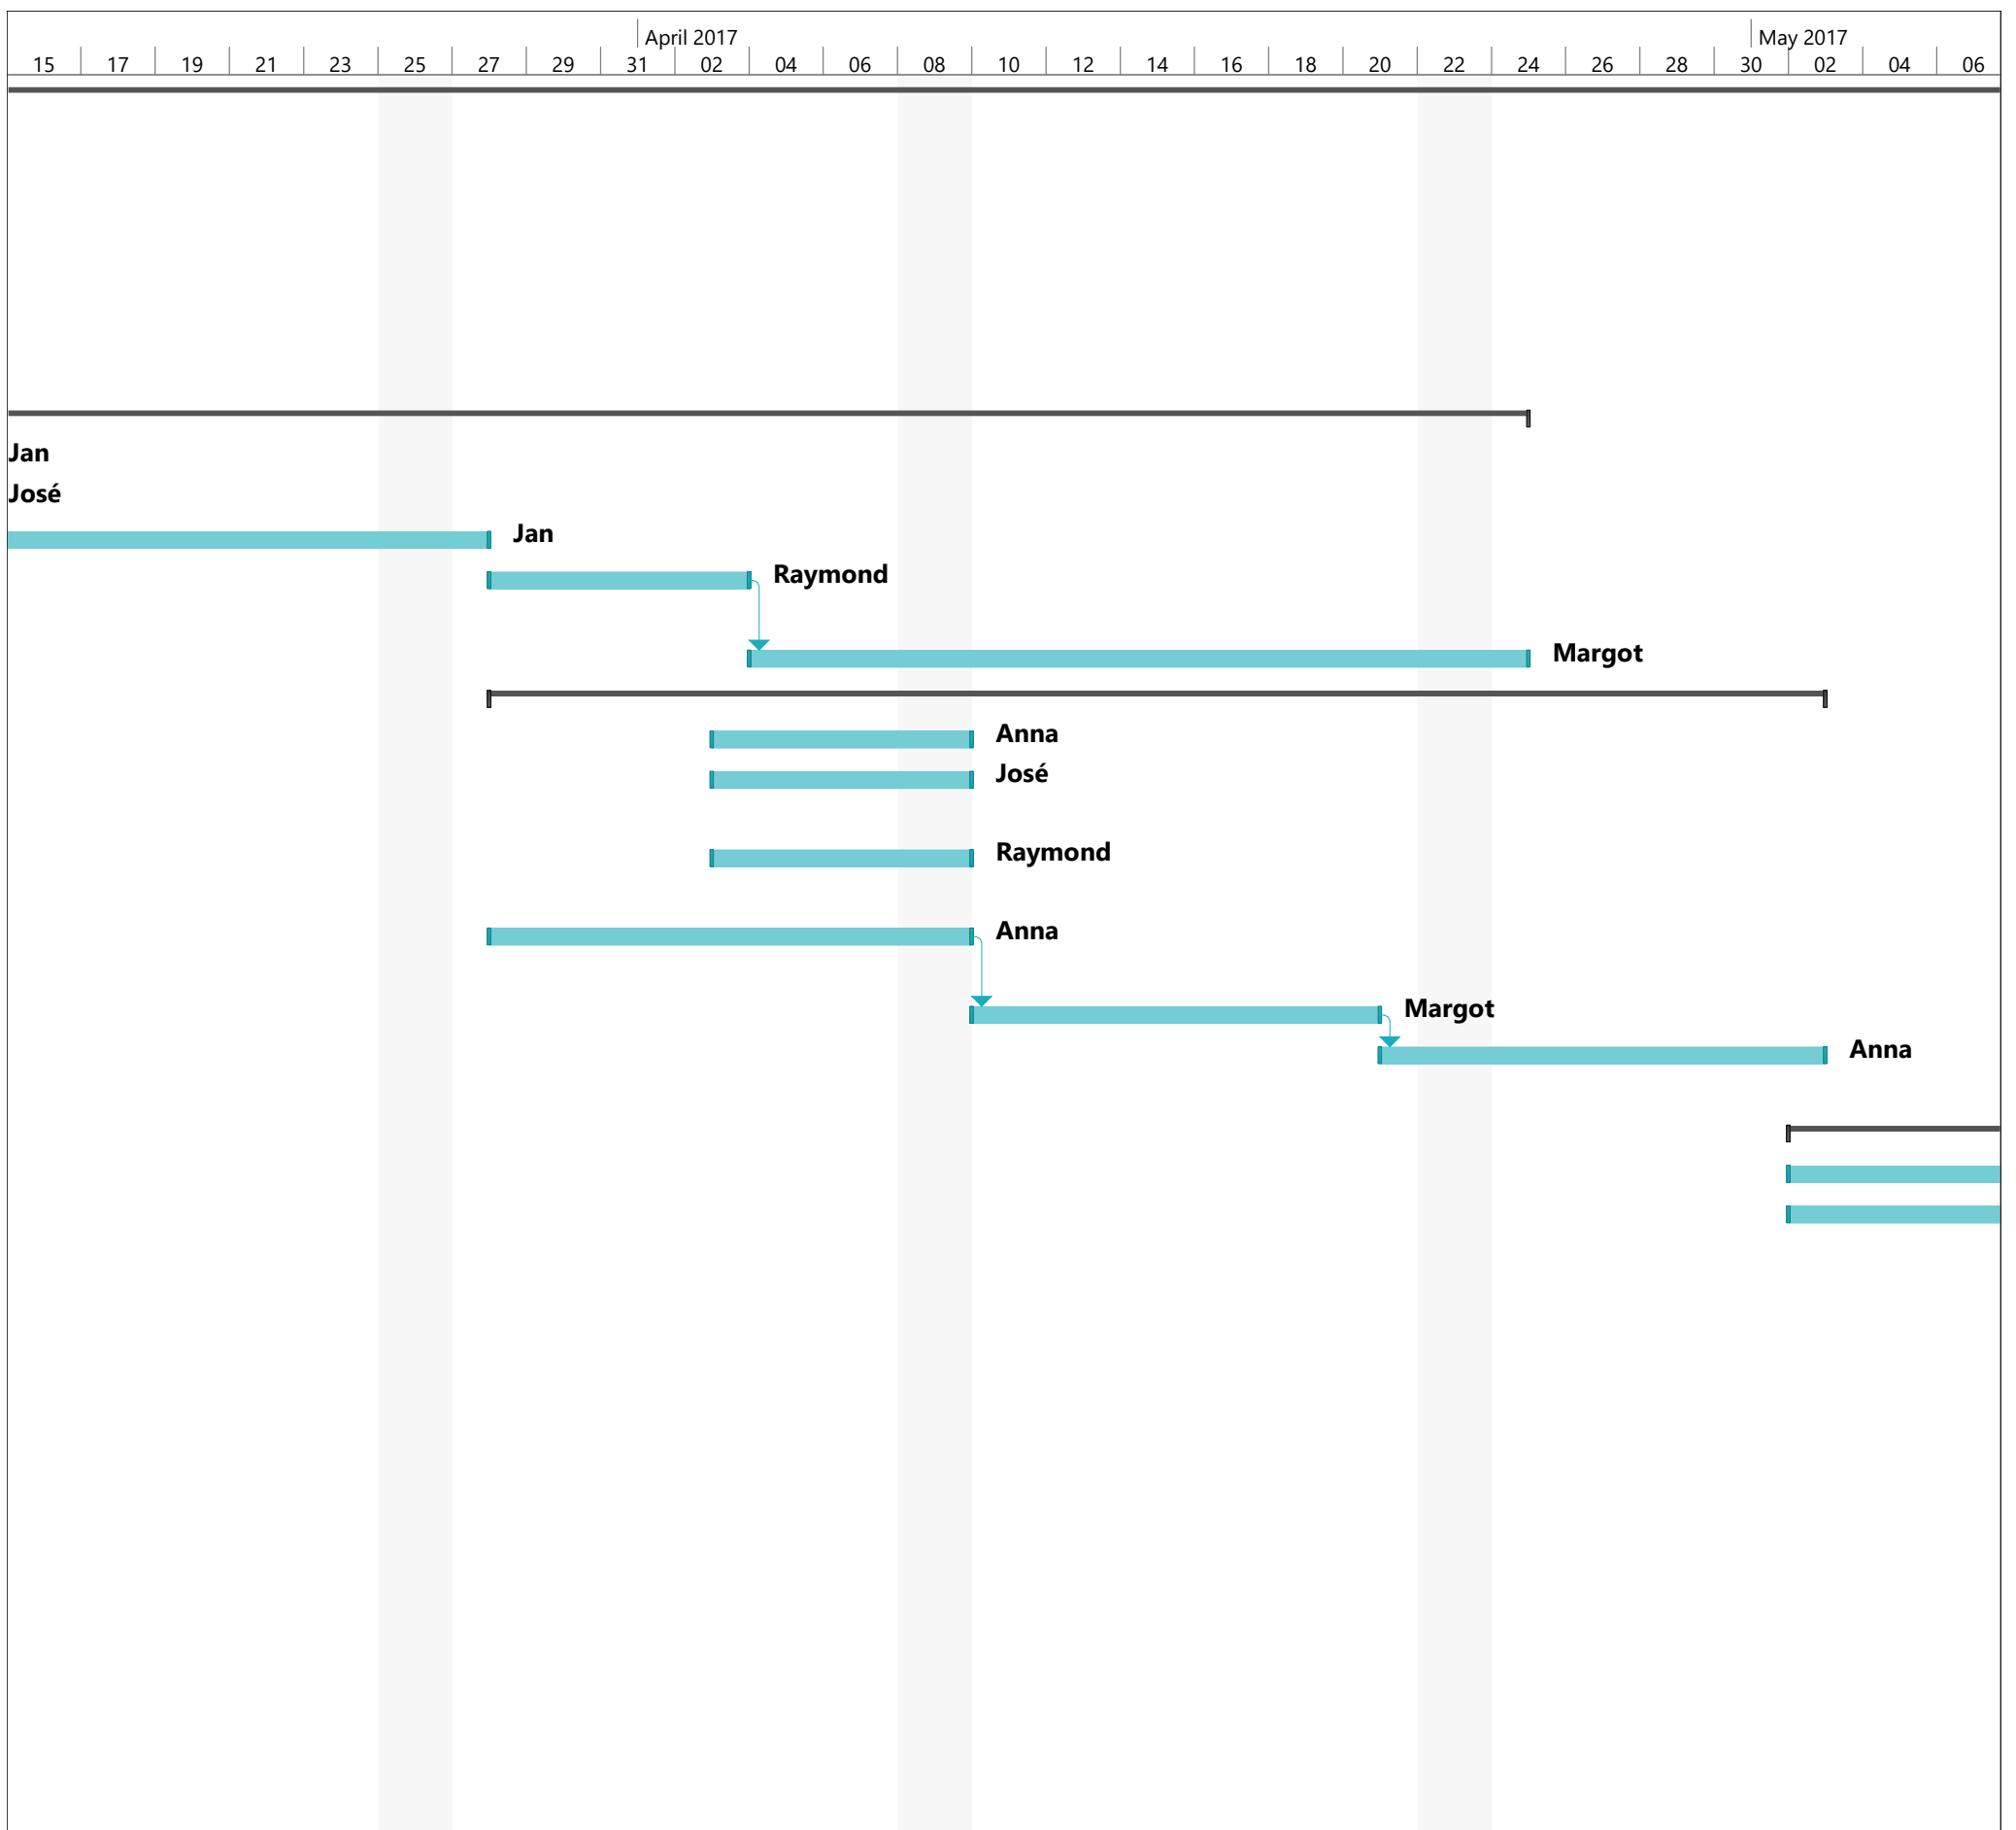

|                                           |                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|-------------------------------------------|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Project: TEAM 3-EPS<br>Date: Fri 03/03/17 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                           | Split              |  | Manual Task           |  | External Milestone |  |
|                                           | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                           | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                           | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                           | Inactive Task      |  | Start-only            |  |                    |                                                                                       |
|                                           | Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

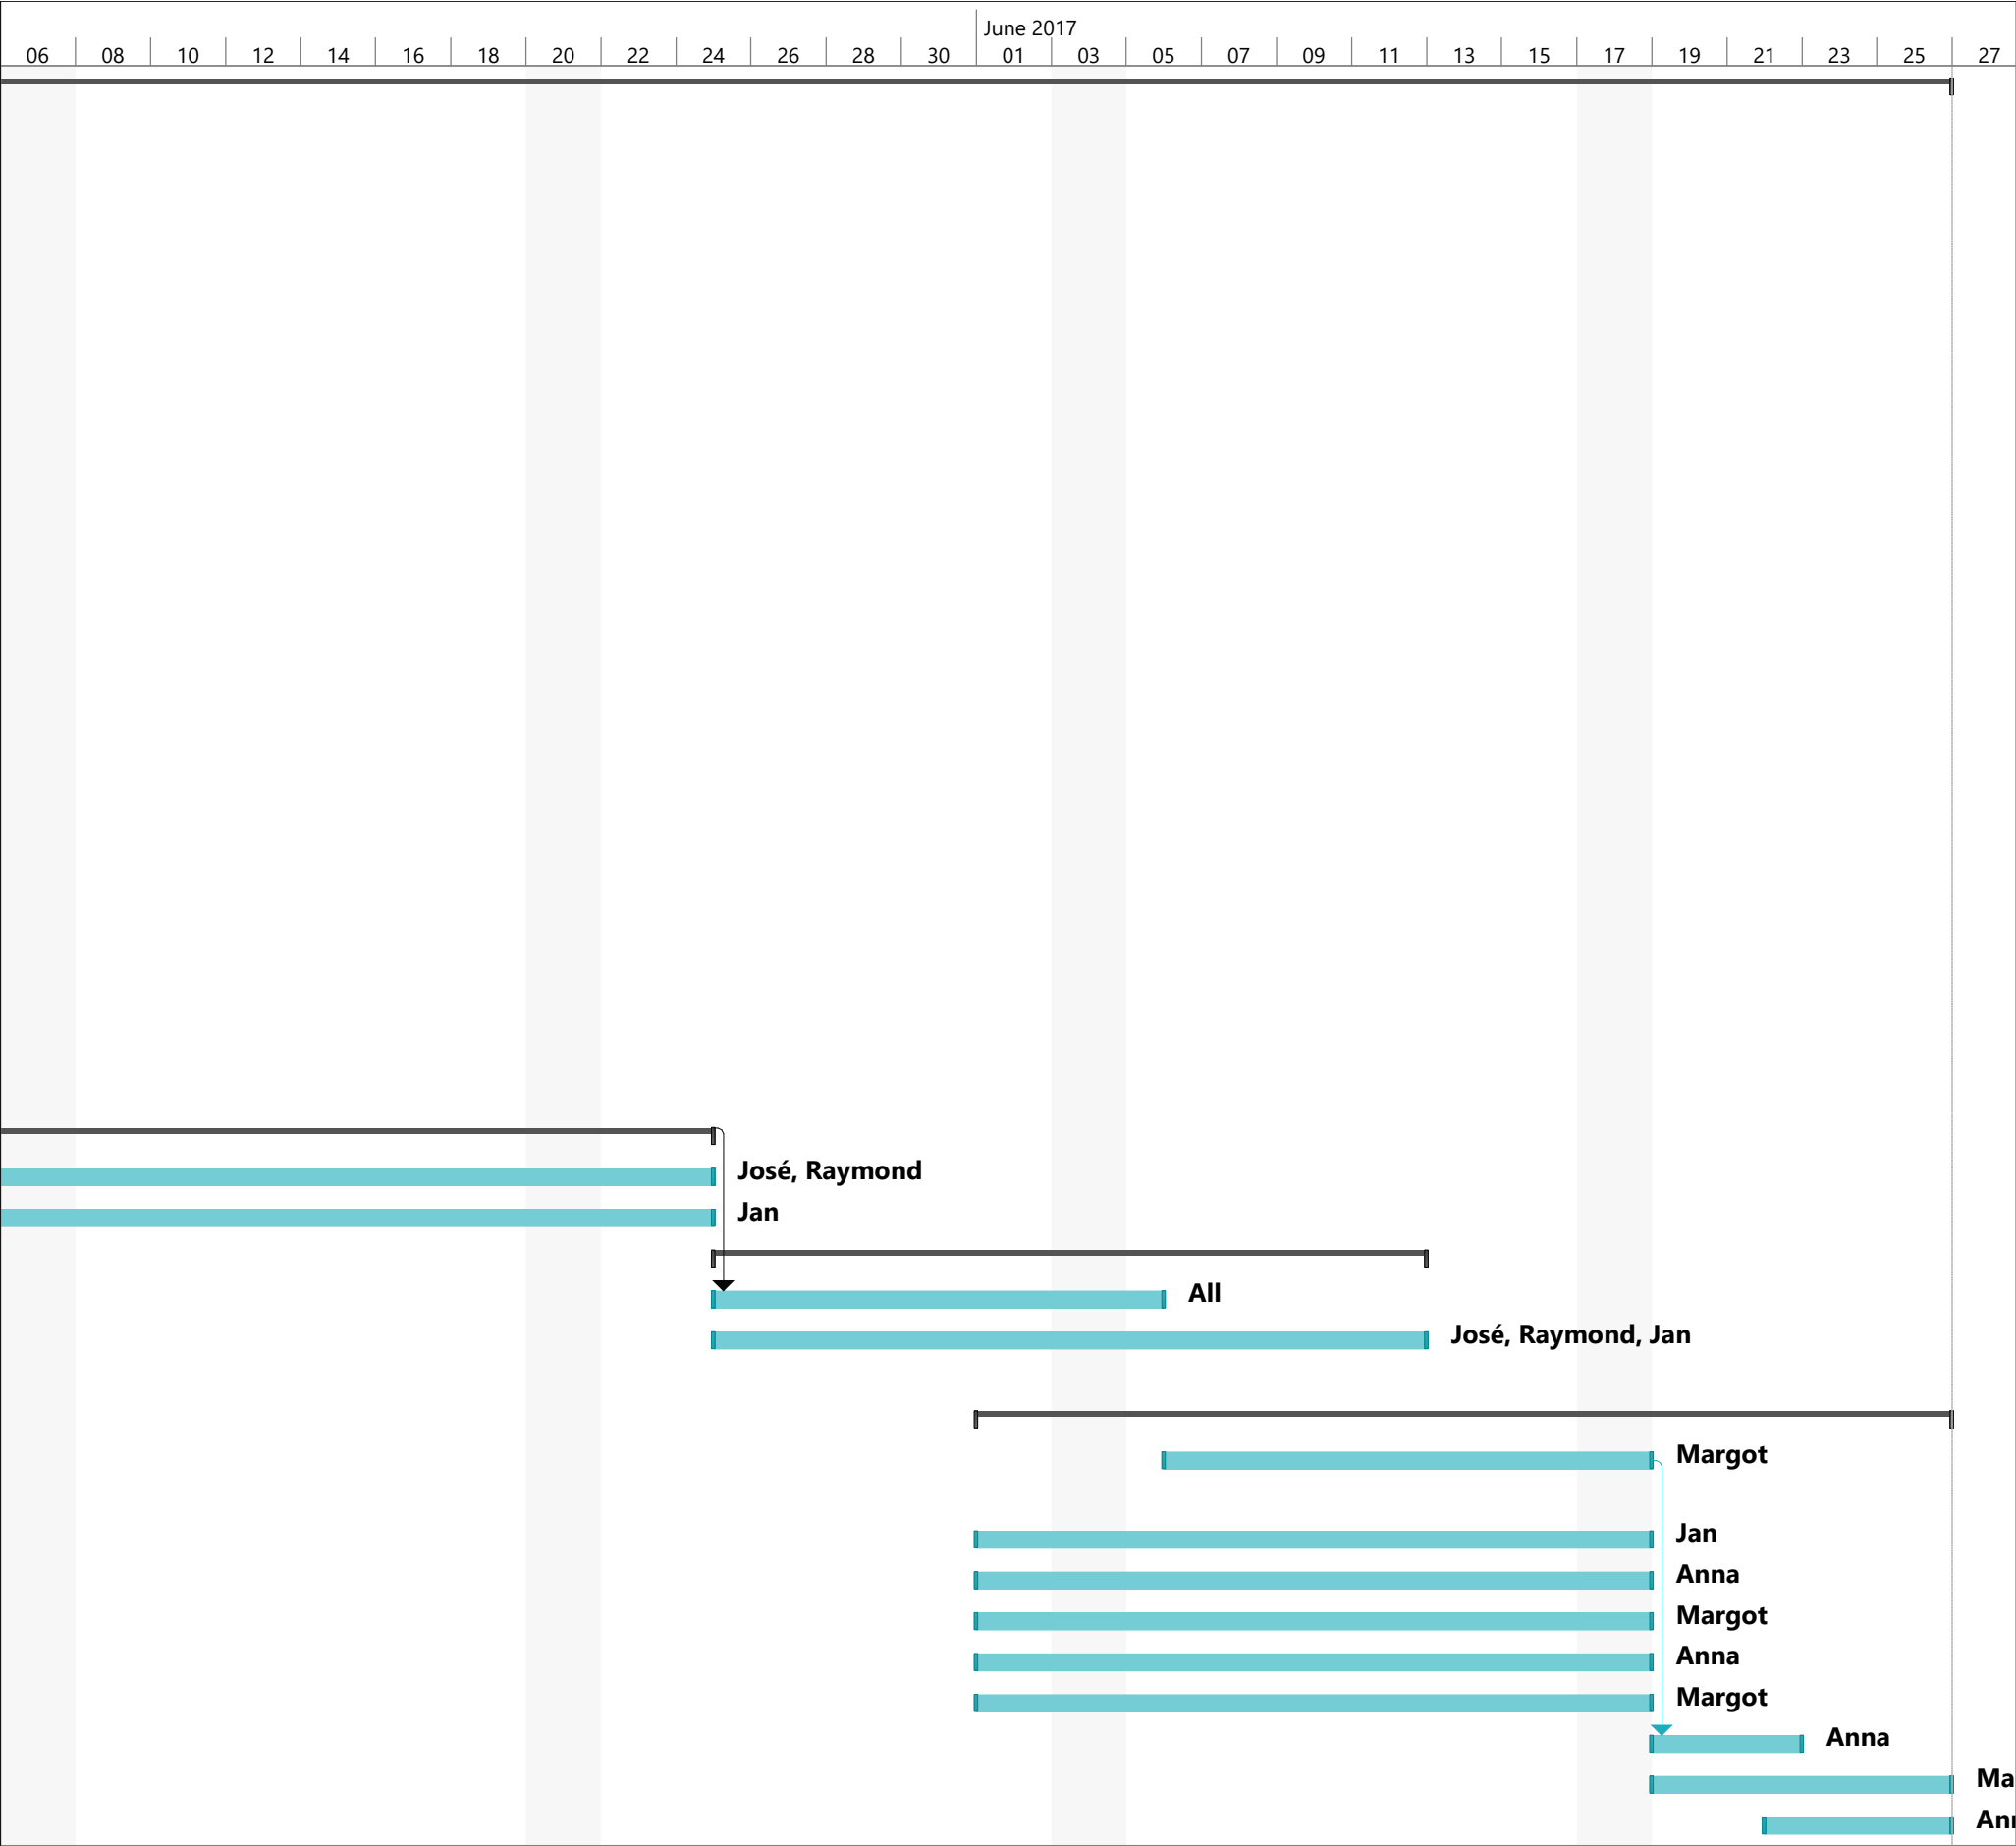

|                                           |                    |  |                       |  |                    |  |
|-------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: TEAM 3-EPS<br>Date: Fri 03/03/17 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                           | Split              |  | Manual Task           |  | External Milestone |  |
|                                           | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                           | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                           | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                           | Inactive Task      |  | Start-only            |  |                    |  |
|                                           | Inactive Milestone |  | Finish-only           |  |                    |  |

